PMO Portfolio Intelligence

PMO overview | synthetic data | as of 30 Sep 2026 | EUR

Overview | Project Details

Department: All | Project Type: All | Project Manager: All | Period: All | Reset Filters


4 of 15 projects Red; 5 report better than the numbers show

91% of allocated hours logged; 2 projects not updated in 30+ days


Forecast cost 7.0% over budget; savings 9.1% below plan

3.73M	7.0%	40.0%	91.2%	93.0%
Total Budget (EUR M)	Cost Variance % (forecast vs budget)	% projects green	Resource Utilization %	Benefit realization % (vs target to date)


Project by Calculated status

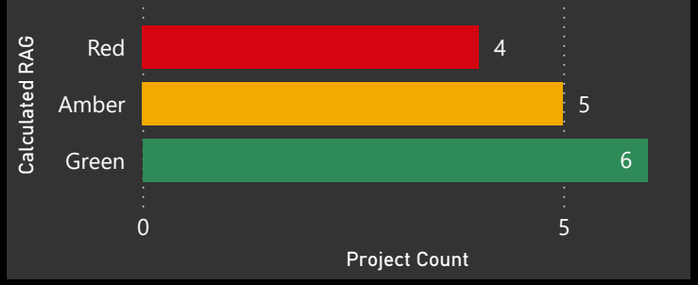

Promised vs forecast annual savings by project (EUR)

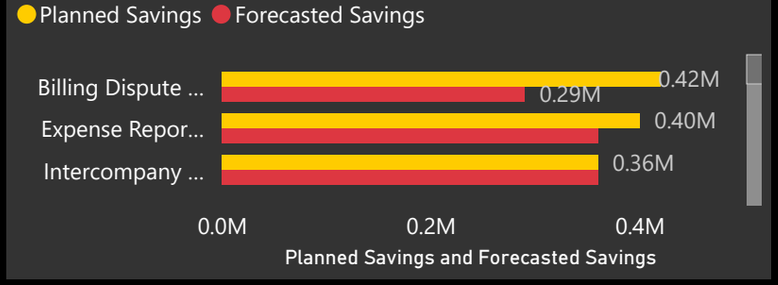


Hours allocated vs hours logged by month

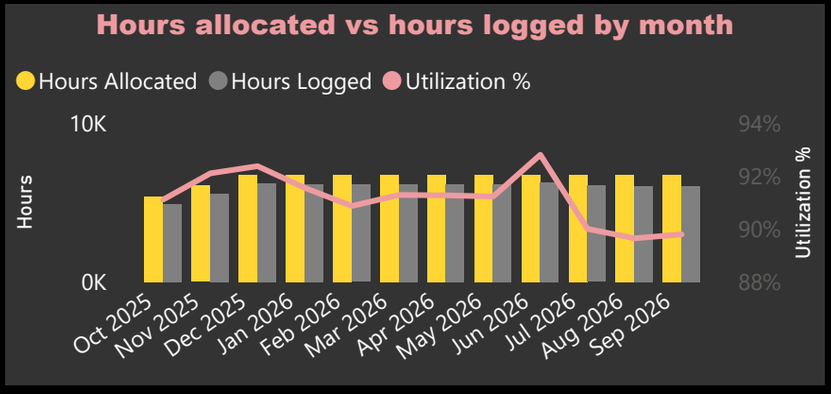

Project_Name | Department | Region | Project_Type | Strategic_Theme

Budget vs Forecast vs Spend to date (EUR)

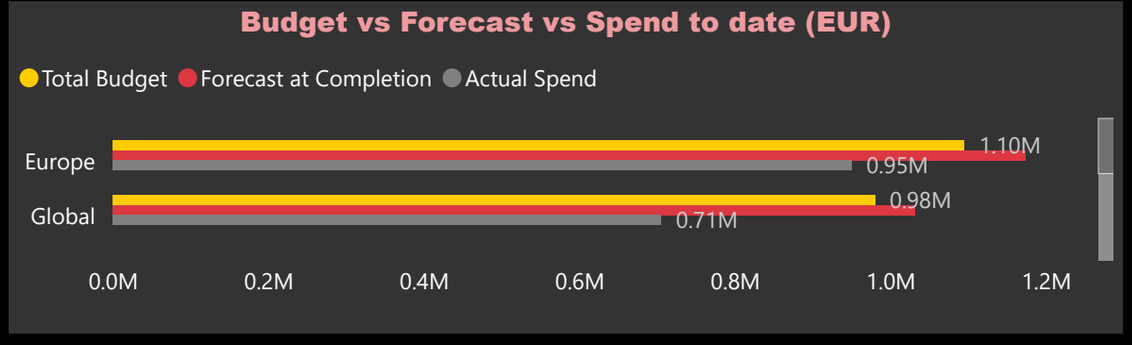

Reported vs Calculated Status Mismatch

Project_Name	Reported_RAG	Calculated RAG	Cost Var %	Days Since Update
Global Reporting Dashboard Refresh	Green	Amber	6.0%	18
Expense Reporting Tool Rollout	Green	Amber	12.0%	22
Customer Credit Note Automation	Green	Amber	9.0%	13
Cash Application Automation	Amber	Red	18.0%	57
Billing Dispute Workflow	Amber	Red	22.0%	43

Synthetic data, not real DHL data. EUR, as of 30 Sep 2026. RAG rule (assumption): Red if cost over budget by more than 15%, slip over 30 days, or savings more than 25% below plan; Amber at 5%, 8 days, 10%.

Project Details

Overview | Project Details

Department: All | Project Type: All | Project Manager: All | Period: All | Reset Filters

Project_Name	Calculated RAG	Cost Var %	Slip Days	Days Since Update	Benefit Status	Status_Comment
Accruals Forecasting Model	Red	4.0%	4	3	Behind	Forecast accuracy below business case; model rework.
Billing Dispute Workflow	Red	22.0%	65	43	Not Yet Live	Integration with billing system re-planned.
Cash Application Automation	Red	18.0%	25	57	Behind	Bank file formats differ by country; extra mapping work
Tax Code Harmonisation	Red	10.0%	45	28	Not Yet Live	Local tax rules differ more than expected.
Customer Credit Note Automation	Amber	9.0%	12	13	At Risk	Scope grew after APAC tax review.
Expense Reporting Tool Rollout	Amber	12.0%	28	22	Not Yet Live	Vendor config delays; go-live still targeted Q4.
Global Reporting Dashboard Refresh	Amber	6.0%	10	18	At Risk	Data refresh issue under review; fix due next sprint.
Month-End Close Harmonisation	Amber	7.0%	20	9	On Track	Two regions still on legacy close calendar.
Vendor Master Data Cleanup	Amber	2.0%	9	5	On Track	Duplicate vendor review slower than planned.
Billing Error Detection Bot	Green	3.0%	5	6	On Track	Minor test delay; no cost impact.
Freight Invoice Audit Automation	Green	-3.0%	0	2	On Track	Audit hit rate above plan.
Intercompany Reconciliation Automation	Green	0.0%	0	1	On Track	Ahead on reconciliation match rate.
Invoice Matching Automation	Green	-2.0%	0	4	On Track	Wave 1 live in 3 countries; wave 2 on plan.
PPM Tool Rollout - Wave 1	Green	4.0%	6	1	On Track	Pilot departments onboarded; training on schedule.
Time Registration Standardisation	Green	1.0%	0	0	On Track	Weekly timesheet deadline agreed with department he
